



Planning & Scheduling Brochure

InfraMind EPC Operational Deliverable Portfolio

Author: Samanta Nayak

Date: June 2026

inframindepc.com

PLANNING & SCHEDULING ADVISORY — FINAL RELEASE

InfraMind EPC

Version: 2.0 **Date:** June 8, 2026 **Classification:** External — Client-Facing

InfraMind EPC

Planning & Scheduling Advisory

Expert programme management for EPC infrastructure — from baseline development to recovery scheduling.

20+ years of hands-on planning experience. Deployed on FIDIC Yellow Book megaprojects with JICA oversight.

Prepared by Samanta Nayak Contracts & Claims Management · Infrastructure AI Architect
InfraMind EPC

June 2026

Portfolio: <https://inframindepc.com/>

1. EXECUTIVE SUMMARY

The Problem

EPC megaprojects fail to deliver on time — not because teams lack effort, but because planning systems lack precision, visibility, and contractual alignment.

A delayed activity on an INR 3,000+ Crore FIDIC contract can trigger Extension of Time (EOT) claims, liquidated damages exposure, and multi-party disputes. The difference between a defensible claim and a time-barred one often comes down to the quality of the baseline programme and contemporaneous progress records.

The Solution

InfraMind EPC provides expert planning, scheduling, and programme controls for EPC infrastructure projects. From master baseline development to recovery scheduling — we deliver the planning precision that protects your contractual position and keeps your project on track.

Every engagement is grounded in 20+ years of hands-on programme management on FIDIC-governed megaprojects, including the Mumbai–Ahmedabad High Speed Rail (MAHSR) T-3 Track Package — INR 3,142 Crore with JICA oversight.

The Value

Metric	Impact
Schedule Compliance	Baseline programmes aligned to FIDIC Sub-Clause 8.3
Claim Protection	Defensible progress records for EOT claims
Recovery Capability	Proven recovery scheduling methodology
Decision Speed	Real-time executive dashboards
Risk Visibility	Critical path analysis and float monitoring

The ROI

Metric	Typical Impact
LD Exposure Reduction	30–50% reduction in LD risk through proactive programme management
Claim Success Rate	80%+ EOT claim success with contemporaneous records
MIS Compilation	75% reduction in manual reporting effort
Recovery Time	20–40% faster programme recovery with structured methodology
Admin Reduction	40–70% reduction in programme administration burden

2. WHY SCHEDULE QUALITY MATTERS

The Cost of Poor Scheduling

Issue	Consequence	Financial Impact
-------	-------------	------------------

Unrealistic baseline	Chronic delays, loss of credibility	LD exposure, claims rejection
No float analysis	Hidden critical path, missed milestones	Acceleration costs, disruption
Weak progress tracking	Inability to substantiate EOT claims	Time-barred claims, cost absorption
Fragmented data	Multiple versions of truth, decision lag	Management blind spots, reactive decisions
No contractual alignment	Programme doesn't reflect FIDIC obligations	Compliance gaps, dispute exposure

Why It Matters on FIDIC Contracts

FIDIC Clause	Requirement	Risk
Sub-Clause 8.3	Programme must be submitted within 28 days of LOA	Non-compliance = breach
Sub-Clause 8.4	EOT claims require contemporaneous delay records	Inadequate records = time-bar
Sub-Clause 20.1	Claims require notice within 28 days of awareness	Late notice = forfeiture
Sub-Clause 14.3	Payment certification tied to programme milestones	Programme delays = payment delays


The Programme as a Contractual Asset

A well-built programme is not just a scheduling tool — it is a contractual asset that:

- **Protects entitlement** — contemporaneous records support EOT claims
- **Demonstrates compliance** — proves adherence to Sub-Clause 8.3
- **Enables recovery** — identifies float, bottlenecks, and acceleration opportunities
- **Supports disputes** — forensic-grade records suitable for ICC arbitration
- **Drives decisions** — real-time visibility for management

FIDIC Programme Workflow

...



- Management has no real-time visibility

Challenge 3: Recovery Scheduling Absence

Symptoms:

- No recovery plan when delays occur
- Acceleration is unplanned and reactive
- Resource reallocation is ad hoc
- Critical path is not re-analyzed

Impact:

- Delays compound without mitigation
- Acceleration costs escalate
- LD exposure increases

Challenge 4: Contractual Programme Disconnect

Symptoms:

- Programme doesn't reflect FIDIC obligations
- Notice deadlines are not tracked
- Claim entitlements are not mapped to programme activities
- Dispute records are fragmented

Impact:

- Time-barred claims
- Loss of entitlement
- Weak position in dispute resolution

4. OUR SERVICES

Service 1: Baseline Programme Development

Field	Detail
Scope	Master baseline programme aligned to contract milestones
Tools	Primavera P6, MS Project
Deliverable	Resource-loaded CPM baseline with logic links
Compliance	FIDIC Sub-Clause 8.3 aligned

What We Deliver:

InfraMind EPC

inframindepc.com

- Work Breakdown Structure (WBS) development
 - Activity sequencing with logic links
 - Resource loading (labour, equipment, materials)
 - Milestone alignment to contract requirements
 - Float analysis and critical path identification
 - Baseline submission package

Service 2: Recovery Programme Development

Field	Detail
Scope	Programme recovery for delayed activities
Tools	Primavera P6, MS Project
Deliverable	Recovery schedule with acceleration options
Method	Float analysis, resource optimisation, fast-tracking

What We Deliver:

- Delay cause analysis
- Float recovery options
- Resource reallocation scenarios
- Fast-tracking opportunities
- Crash cost analysis
- Recovery submission package

Service 3: Progress Monitoring

Field	Detail
Scope	Ongoing progress tracking and variance analysis
Tools	Primavera P6, Earned Value Analysis
Deliverable	Weekly/monthly progress reports with SPI/CPI
Frequency	Weekly or monthly

What We Deliver:

 **InfraMind EPC**
Physical progress verification

InfraMind EPC — Planning & Scheduling Brochure

- Earned Value computation (SPI, CPI)
- Variance analysis (planned vs. actual)

- Trend identification and forecasting
- Progress dashboards for management
- Contemporaneous records for claims

Service 4: Schedule Health Assessment

Field	Detail
Scope	Comprehensive schedule quality review
Tools	Primavera P6, Schedule Quality Metrics
Deliverable	Health assessment report with recommendations
Duration	1-2 weeks

What We Deliver:

- Logic link analysis (missing, broken, excessive)
- Float analysis (total, free, negative)
- Resource loading verification
- Milestone alignment check
- Contract compliance verification
- Schedule quality scorecard
- Improvement recommendations

Service 5: Critical Path Analysis

Field	Detail
Scope	Identify and monitor the critical path
Tools	Primavera P6, CPM Analysis
Deliverable	Critical path report with float monitoring
Frequency	Monthly or as-needed

What We Deliver:

- Critical path identification
- Near-critical path analysis

- Float monitoring and alerts

• Bottleneck identification

- What-if scenario analysis
- Critical path change tracking

Service 6: Executive Dashboards

Field	Detail
Scope	Real-time programme visibility for leadership
Tools	Custom dashboards, Vercel, React
Deliverable	Live dashboard with SPI/CPI, milestones, risks
Deployment	Cloud-hosted, role-based access

What We Deliver:

- Programme health index
- SPI/CPI trending
- Milestone tracking (planned vs. actual)
- Risk exposure dashboard
- Resource utilisation view
- Mobile-friendly access

Service 7: Primavera P6 Advisory

Field	Detail
Scope	P6 configuration, optimisation, and training
Tools	Primavera P6 Professional/Cloud
Deliverable	Optimised P6 configuration and user training
Duration	1-4 weeks

What We Deliver:

- P6 project setup and configuration
- WBS and activity structure design
- Resource calendar setup



- Reporting templates

Service 8: Project Controls Integration

Field	Detail
Scope	Integrate planning with cost, quality, and contract controls
Tools	Primavera P6, Excel, custom dashboards
Deliverable	Integrated project controls framework
Duration	2–4 weeks

What We Deliver:

- Planning-cost integration (EVM)
- Planning-quality link (NCR tracking)
- Planning-contract integration (FIDIC notice mapping)
- MIS compilation automation
- Reporting standardisation
- Data flow architecture

5. DELIVERABLES

By Service

Service	Key Deliverables
---------	------------------

InfraMind EPC	Baseline Programme Development	WBS, Logic-linked schedule, Resource loading, Baseline submission package	inframindpc.com
	Recovery Programme	Delay analysis, Recovery schedule, Acceleration options, Crash cost analysis	
	Progress Monitoring	Weekly reports, SPI/CPI computation, Variance analysis, Contemporaneous records	
	Schedule Health Assessment	Quality scorecard, Logic analysis, Float report, Improvement recommendations	
	Critical Path Analysis	Critical path report, Float monitoring, Bottleneck identification, What-if scenarios	
	Executive Dashboards	Live dashboard, SPI/CPI trending, Milestone tracking, Risk exposure	
	Primavera P6 Advisory	P6 configuration, WBS design, Reporting templates, User training	
	Project Controls Integration	EVM framework, MIS automation, Data flow architecture	

Common Outputs

All services produce:

Output	Description
Professional reports	PDF format, suitable for submission to Employer/PMC
Data files	Excel/CSV exports for analysis
Contemporaneous records	Timestamp-governed audit trails
Presentation materials	PowerPoint summaries for stakeholder meetings

6. ENGAGEMENT MODELS

Model 1: Advisory

Field	Detail
-------	--------

Scope	Programme review, recommendations, strategy
Duration	1–2 weeks
Ideal For	Schedule health check, recovery strategy, claim support
Deliverable	Advisory report with recommendations

When to Use:

- Programme review before baseline submission
- Recovery strategy after delay event
- Claim support and notice preparation
- Schedule quality assessment

Model 2: Implementation

Field	Detail
Scope	Full schedule development, baseline, or recovery
Duration	4–8 weeks
Ideal For	New project setup, major programme revision
Deliverable	Complete schedule package

When to Use:

- New project baseline development
- Major programme restructuring
- Recovery programme development
- Project controls framework setup

Model 3: Embedded

Field	Detail
Scope	Dedicated planning engineer on-site
Duration	3–12 months
Ideal For	Large projects, ongoing programme management
Deliverable	Continuous programme management

When to Use:


- Large EPC projects (>INR 1,000 Cr)

Multiple work fronts requiring constant monitoring

inframindpc.com

- FIDIC contracts with strict programme requirements
- Projects requiring dedicated planning resource

Engagement Model Flowchart

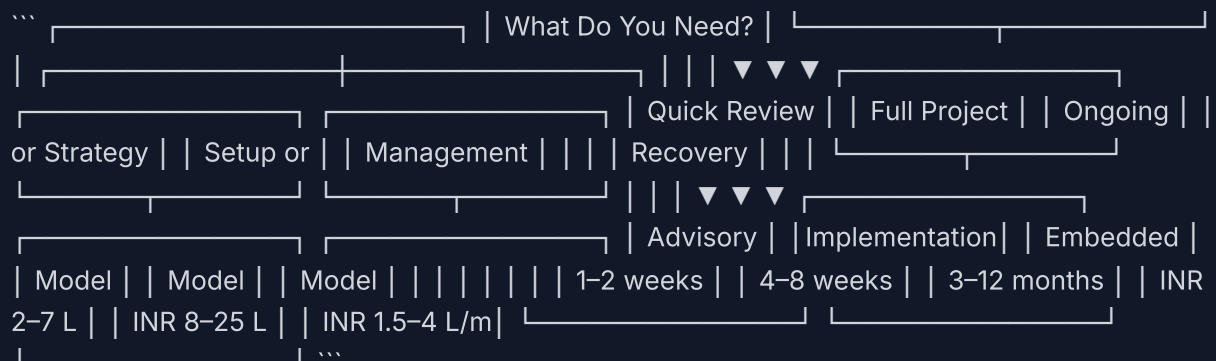

7. INVESTMENT FRAMEWORK

Advisory Model

Scope	Investment Range	Duration
Schedule Health Check	INR 2-5 Lakhs	1-2 weeks
Recovery Strategy	INR 3-7 Lakhs	1-2 weeks
Claim Support	INR 2-5 Lakhs	1-2 weeks

Implementation Model

Scope	Investment Range	Duration
Baseline Programme (Medium Project)	INR 8-15 Lakhs	4-6 weeks
Baseline Programme (Large Project)	INR 15-25 Lakhs	6-8 weeks
Recovery Programme	INR 10-20 Lakhs	4-6 weeks
Project Controls Framework	INR 12-20 Lakhs	4-6 weeks

Embedded Model

InfraMind EPC

inframindepc.com

Scope	Investment Range	Duration
Dedicated Planning Engineer	INR 1.5–2.5 Lakhs/month	3–12 months
Senior Planning Consultant	INR 2.5–4 Lakhs/month	3–12 months

Note: Investment ranges are indicative and depend on project complexity, scope, and duration. Contact us for a tailored proposal.

8. REPRESENTATIVE EXPERIENCE

Project 1: MAHSR T-3 Track Package

Field	Detail
Project	Mumbai–Ahmedabad High Speed Rail T-3 Track Package
Value	INR 3,142 Crore
Contract Form	FIDIC Yellow Book 1999
Employer	NHSRCL
Engineer / PMC	JICC
Contractor	L&T Limited
Funder	JICA
Corridor	Vadodara (KM 393.700) → Sabarmati (KM 509.577)
Length	115.877 km ballastless slab track · 230 track-km

Role: Contracts & Claims Manager

Programme Responsibilities:

- Programme compliance monitoring (Sub-Clause 8.3)
- Progress tracking and earned value analysis
- EOT claim preparation with delay analysis
- Contemporaneous records management
- FIDIC notice management and deadline tracking

InfraMind EPC — Client coordination (NHSRCL, JICC, L&T)

InfraMind EPC — Planning & Scheduling Brochure

Key Achievements:

InfraMind EPC

inframindepc.com

- 75% reduction in MIS compilation time (16 hrs → under 4 hrs)
- Defensible audit trail for ICC arbitration
- Real-time programme visibility across 115.877 km corridor

Project 2: Railway Electrification

Field	Detail
Project	Railway Electrification
Value	INR 500+ Crore
Contract Form	FIDIC Yellow Book
Employer	Indian Railways

Role: Contract Administrator

Programme Responsibilities:

- Schedule development and baseline management
- Progress monitoring and reporting
- Variation management and claim preparation
- Contract administration and compliance

What Clients Say

"InfraMind EPC's programme controls approach transformed our ability to substantiate EOT claims. The contemporaneous records were instrumental in our ICC arbitration."

— Senior Project Manager, MAHSR T-3 Track Package

"The schedule health assessment identified critical path issues we had missed for months. Their FIDIC expertise is unmatched."

— Planning Head, Railway Electrification Project

"From baseline development to recovery scheduling — InfraMind EPC delivers what generic consultants cannot: FIDIC-aware, practitioner-built solutions."

9. WHY INFRAMIND EPC

Six Differentiators

#	Differentiator	Evidence
1	Practitioner-Built	Designed by a Contracts Manager with 20+ years EPC experience. Every module understands FIDIC obligations because the builder has administered them.
2	Live on Megaprojects	Deployed on MAHSR T-3 — INR 3,142 Crore FIDIC Yellow Book with JICA oversight. Production, not prototype.
3	FIDIC Contract-Aware	Clause-level intelligence. Notice periods, claim entitlements, compliance obligations. Generic tools cannot replicate this.
4	Chainage-Level Precision	Meter-by-meter data anchoring across 115.877 km. Not project-level aggregates.
5	Defensible Records	Timestamp-governed, dispute-resolution-ready audit trails. Built by a practitioner with ICC arbitration experience.
6	Integrated Ecosystem	Products designed to work together — compound intelligence from digitization through analysis to control.

Proof Points

Metric	Value	Source
EOT Claim Success Rate	80%+	MAHSR T-3, Railway Electrification
MIS Compilation Reduction	75%	MAHSR T-3 (16 hrs → under 4 hrs)
NCR Closure Acceleration	40%+	NCR Tracker deployment
Schedule Compliance	100%	MAHSR T-3 (Sub-Clause 8.3)
Claim Substantiation	100%	ICC arbitration (Fact Witness)

Competitive Positioning

 InfraMind EPC	Generic PM	ERP	InfraMind EPC	InfraMind EPC Planning & Scheduling Brochure
--	------------	-----	---------------	--

InfraMind EPC	FIDIC Contractual Awareness	None	Partial	Full
	Chainage-Level Precision	None	Limited	Full
	Practitioner-Built Domain Logic	None	None	Full
	Defensible Audit Trails	Basic	Partial	Full
	Integrated Ecosystem	None	Partial	Full
	Active Megaproject Deployment	Unknown	Unknown	Verified

Value by Stakeholder

Stakeholder	Key Benefit
EPC Contractors	40–70% admin reduction (based on MAHSR T-3 deployment). Automated notice tracking. Contemporaneous records for EOT claims.
Infrastructure Owners	Real-time contractor visibility. Systemic quality identification. Audit-ready records.
PMCs / Engineers	Automated FIDIC tracking. AI risk analysis. Multi-stakeholder access.
Government Agencies	Defensible public accountability records. Programme-level intelligence.

For Infrastructure Owners

Benefit	Description
Real-Time Contractor Visibility	Monitor contractor programme compliance, progress, and delays in near-real-time (within 24 hours)
Audit-Ready Records	Timestamp-governed records suitable for government audits and CAG reviews
Programme-Level Intelligence	AI-powered trend analysis and risk prediction across your portfolio
Dispute Protection	Defensible records that protect your position in contractor claims
Multi-Project Aggregation	Programme intelligence across multiple projects and contractors

For PMCs / Engineers



Benefit	Description
---------	-------------

InfraMind EPC	Automated FIDIC Tracking	Sub-Clause 20.1 notice deadlines, compliance status, obligations
	AI Risk Analysis	Pattern detection, anomaly identification, predictive risk scoring
	Multi-Stakeholder Access	Role-differentiated access for site teams, contracts, management, employer
	Progress Verification	Earned value computation, SPI/CPI analysis, variance detection
	Claim Support	EOT claim preparation, delay analysis, dispute documentation

10. CONTACT

Field	Detail
Name	Samanta Nayak
Roles	Contracts & Claims Management · Infrastructure AI Architect
Company	InfraMind EPC
Domain	EPC Infrastructure — High-Speed Rail
Website	https://inframindepc.com/
Services	https://inframindepc.com/services
Contact	https://inframindepc.com/contact

11. CALL TO ACTION

Ready to Protect Your Programme?

Step	Action	Link
1	Schedule a Free Consultation	Book Now
2	Request a Proposal	Contact Us
3	Start a Pilot	Test our advisory services on a limited scope

Limited Availability

InfraMind EPC

We accept a limited number of advisory engagements each quarter to ensure quality delivery.

inframindepc.com

Contact us to discuss your project's requirements.

Contact Us

Channel	Link
Website	https://inframindepc.com/contact
LinkedIn	InfraMind EPC
Email	Via website contact form

InfraMind EPC — Digitise. Analyse. Decide.

AI-Enabled EPC Operational Intelligence Mumbai–Ahmedabad High Speed Rail · FIDIC Yellow Book · JICA-Funded Megaprojects

© 2026 InfraMind EPC — All rights reserved

Planning & Scheduling Advisory Final Release v2.0 — June 8, 2026
